

Suppression Repair

Beachie Creek
ORWIF-200299
Beachie 2

Riverside
ORMHF-000859
Beachie 2



10/13/20
Page: 9

- Division Break
- Drop Point
- Repeater
- Unknown
- Fire Station
- State Highway
- County Road
- Major road
- Intermediate road
- Minor road
- Decommissioned or Closed
- BPA Transmission Lines
- County Boundary
- Structures
- Completed Dozer Line
- Completed Hand Line
- Road as Completed Line
- Access or Improved Road
- Line Break Completed
- Other
- Unknown
- Completed - Inspected
- In Use - Fire Management
- Completed - Ready for Inspection
- In Progress
- Repair Needed
- Other - See Comments
- Unknown
- Wildfire Daily Fire Perimeter
- Bureau of Land Management
- State
- Private/Unknown

| FC Point Type | Repair Status | Repair Comments | Label |
|---------------|---------------|-----------------|----------|
| Drop Point | Unknown | | DP-15 |
| Drop Point | Unknown | | DP-16 |
| Drop Point | Unknown | | DP-18 |
| Drop Point | Unknown | | DP-20 |
| Drop Point | Unknown | | DP-28 |
| Drop Point | Unknown | | DP-29 |
| Drop Point | Unknown | | DP-31 |
| Drop Point | Unknown | | DP-33 |
| Drop Point | Unknown | | DP-35 |
| Drop Point | Unknown | | DP-36 |
| Repeater | Unknown | | CMD B-10 |
| Repeater | Unknown | | L6 HUB |

| FC Line Type | Repair Status | Repair Comments | Length Feet |
|------------------------|----------------------------------|---|-------------|
| Unknown | In Use - Fire Management | | 472 |
| Unknown | In Use - Fire Management | | 2383 |
| Unknown | In Use - Fire Management | | 2524 |
| Road as Completed Line | Unknown | | 183 |
| Road as Completed Line | Unknown | | 246 |
| Road as Completed Line | Unknown | | 441 |
| Road as Completed Line | Unknown | | 446 |
| Road as Completed Line | Unknown | | 500 |
| Road as Completed Line | Unknown | | 601 |
| Road as Completed Line | Unknown | | 606 |
| Road as Completed Line | Unknown | Pull flagging | 751 |
| Road as Completed Line | Unknown | | 772 |
| Road as Completed Line | Unknown | | 831 |
| Road as Completed Line | Unknown | | 831 |
| Road as Completed Line | Unknown | | 889 |
| Road as Completed Line | Unknown | | 889 |
| Road as Completed Line | Unknown | | 899 |
| Road as Completed Line | Unknown | | 2817 |
| Road as Completed Line | Repair Needed | Created some roadside berms | 686 |
| Road as Completed Line | Repair Needed | Open berms on downhill side to allow drainage | 1371 |
| Road as Completed Line | Repair Needed | Created some roadside berms, pre-existing drainage issues, consult landowner | 3158 |
| Road as Completed Line | Other - See Comments | | 3581 |
| Road as Completed Line | Completed - Ready for Inspection | Water crossings should be inspected | 199 |
| Road as Completed Line | Completed - Ready for Inspection | Some erosion problems at the S end. The rest looks good except for water crossing. | 4147 |
| Other | Unknown | Determine if this was put up for fire or if flagged for another non fire reason. If fire related pull flagging. | 278 |
| Other | Unknown | | 720 |
| Other | Unknown | | 1578 |
| Line Break Completed | Unknown | | 476 |
| Line Break Completed | Unknown | | 1322 |
| Line Break Completed | Unknown | | 1890 |
| Line Break Completed | Unknown | | 1890 |
| Line Break Completed | Unknown | | 2109 |
| Line Break Completed | Unknown | | 2109 |
| Line Break Completed | Unknown | | 207 |
| Completed Hand Line | Unknown | | 405 |
| Completed Hand Line | Repair Needed | Construct water bars and cover with slash in accordance with suppression repair plan | 195 |
| Completed Hand Line | Repair Needed | Install water bars | 224 |
| Completed Hand Line | Repair Needed | repair per local unit specs | 321 |
| Completed Hand Line | Repair Needed | handline | 421 |
| Completed Hand Line | Repair Needed | repair per local unit specs | 464 |
| Completed Hand Line | Completed - Ready for Inspection | Handline along edge of burn. Needs repair. Pull flagging, pull in berms, brush and water bars needed on the steep slope sections of line. | 1922 |
| Completed Hand Line | Completed - Ready for Inspection | Pull flagging, maybe a few water bars, pull in and brush short sections of berm. | 1932 |
| Completed Hand Line | Completed - Inspected | Water bars installed. | 623 |
| Completed Hand Line | Completed - Inspected | Water bars installed. | 771 |
| Completed Hand Line | Completed - Inspected | Water bars installed. | 1155 |
| Completed Hand Line | Completed - Inspected | Water bars installed. | 1633 |
| Completed Dozer Line | Unknown | | 499 |
| Completed Dozer Line | Unknown | | 513 |
| Completed Dozer Line | Unknown | | 649 |
| Completed Dozer Line | Unknown | | 723 |
| Completed Dozer Line | Unknown | | 902 |
| Completed Dozer Line | Repair Needed | | 902 |
| Completed Dozer Line | Repair Needed | | 902 |

| FC Line Type | Repair Status | Repair Comments | Length Feet |
|----------------------|----------------------------------|--|-------------|
| Completed Dozer Line | Repair Needed | Obtainate berm, need medium excavator with grapple bucket | 116 |
| Completed Dozer Line | Repair Needed | repair per local unit specs | 116 |
| Completed Dozer Line | Repair Needed | | 256 |
| Completed Dozer Line | Repair Needed | Consult with landowner | 290 |
| Completed Dozer Line | Repair Needed | repair per local unit specs | 291 |
| Completed Dozer Line | Repair Needed | Replace logs to block access. Placement | 311 |
| Completed Dozer Line | Repair Needed | Repair per local unit specs | 443 |
| Completed Dozer Line | Repair Needed | Construct water bars and/or dips in accordance with suppression repair plan | 502 |
| Completed Dozer Line | Repair Needed | Construct water bars, pull back berm. Consult private land owner. | 527 |
| Completed Dozer Line | Repair Needed | | 865 |
| Completed Dozer Line | Repair Needed | Discuss existing road with land owner if possible | 1135 |
| Completed Dozer Line | Repair Needed | consult landowner, likely needs medium excavator | 1472 |
| Completed Dozer Line | Repair Needed | Water bars don't have lead out | 1793 |
| Completed Dozer Line | Repair Needed | | 1921 |
| Completed Dozer Line | Repair Needed | Repair per local BLM specs, elaborate berm and push piles, water bar as needed, needs medium excavator with grapple claw, access through private land to south | 2202 |
| Completed Dozer Line | Repair Needed | | 2422 |
| Completed Dozer Line | Repair Needed | | 2594 |
| Completed Dozer Line | Repair Needed | Some boggy areas with a dozer trench. | 4355 |
| Completed Dozer Line | Repair Needed | Some boggy areas with a dozer trench. | 4355 |
| Completed Dozer Line | Repair Needed | water bars as needed, elaborate berm and dozer paths. | 5411 |
| Completed Dozer Line | In Progress | | 627 |
| Completed Dozer Line | Completed - Ready for Inspection | Install water bars, pull berm and slash back. Recommend inaccurate. (Waterbar completed by hand 10/4) | 132 |
| Completed Dozer Line | Completed - Ready for Inspection | | 193 |
| Completed Dozer Line | Completed - Ready for Inspection | | 250 |
| Completed Dozer Line | Completed - Ready for Inspection | Repair per local unit specs | 256 |
| Completed Dozer Line | Completed - Ready for Inspection | Repair per local unit specs | 422 |
| Completed Dozer Line | Completed - Ready for Inspection | | 486 |
| Completed Dozer Line | Completed - Ready for Inspection | unsure what can be done. The line follows a road bed cut through a hill. Any outflow will end up in a rock quarry. | 506 |
| Completed Dozer Line | Completed - Ready for Inspection | Pull berm back. Pull slash across dozer line. | 538 |
| Completed Dozer Line | Completed - Ready for Inspection | | 551 |
| Completed Dozer Line | Completed - Ready for Inspection | | 574 |
| Completed Dozer Line | Completed - Ready for Inspection | Water bars needed | 574 |
| Completed Dozer Line | Completed - Ready for Inspection | Open downhill berms where possible | 840 |
| Completed Dozer Line | Completed - Ready for Inspection | Pull back berm, construct water bars and/or dips in accordance with suppression repair plan | 1072 |
| Completed Dozer Line | Completed - Ready for Inspection | repair per local unit specs needs water bars at end of line | 1127 |
| Completed Dozer Line | Completed - Ready for Inspection | Eliminate berm and push piles, pull slash over line, no need for water bars | 1132 |
| Completed Dozer Line | Completed - Ready for Inspection | repair to local unit specs | 1603 |
| Completed Dozer Line | Completed - Ready for Inspection | | 1594 |
| Completed Dozer Line | Completed - Ready for Inspection | | 1686 |
| Completed Dozer Line | Completed - Ready for Inspection | repair per unit specs, will need excavator with grapple bucket | 1735 |
| Completed Dozer Line | Completed - Ready for Inspection | line on old road bed, scatter slash back on line, will need excavator with grapple bucket | 1739 |
| Completed Dozer Line | Completed - Ready for Inspection | Consult landowner | 3219 |
| Completed Dozer Line | Completed - Ready for Inspection | Constructed with excavator, big cuts and some wet areas. | 4138 |
| Completed Dozer Line | Completed - Ready for Inspection | Install additional water bars. Could be done with dozer | 4172 |
| Completed Dozer Line | Completed - Inspected | | 222 |
| Completed Dozer Line | Completed - Inspected | | 480 |
| Completed Dozer Line | Completed - Inspected | Water bars installed and access blocked. | 548 |
| Completed Dozer Line | Completed - Inspected | | 785 |
| Completed Dozer Line | Completed - Inspected | | 836 |
| Completed Dozer Line | Completed - Inspected | | 831 |

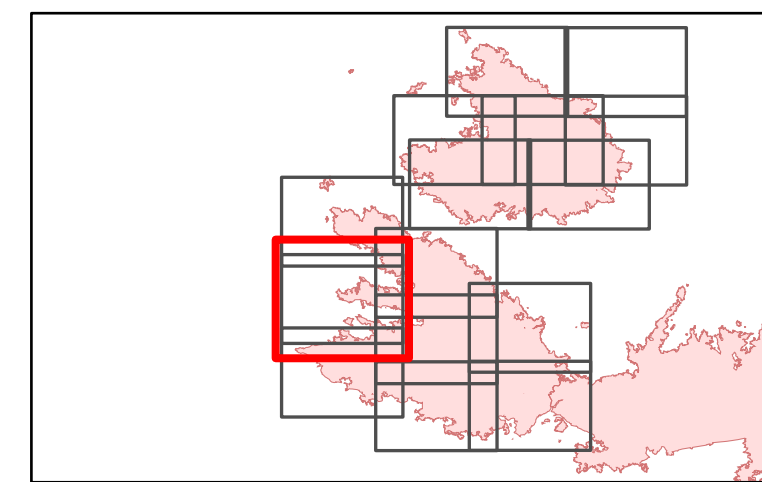

1:33,000 - 10/12/2020 2037
Acres from GIS
North American 1983 Datum, LatLong Grid

