Suppression Repair Tiles

Cedar Creek
OR-WIF-220180
10/23/2022 24 Hour
127,883 acres at 10/20/2022 @ 2027
1:1,100,000

Div P2

Accountable Property - Repair Status
- In Use - Fire Management (8)
- Completed - Inspected (2)

Accountable Property
- Other Property (6)
- Pump (1)
- Water Tank (3)

- In Use - Fire Management (10)
- Repair Needed (19)
- Completed - Ready for Inspection (1)
- Completed - Inspected (43)

- Sling Site (4)
- Drop Point (1)
- Value at Risk (3)
- Other (1)
- Gate (2)
- Structure Wrap (9)
- Road Repair (4)
- Repair Point (29)
- Landing or Log Deck (3)
- Dozer Push (15)
- Culvert (1)
- Safety Zone (1)

- Completed Dozer Line (16)
- Completed Hand Line (33)
- Completed Road as Line (5)
- Road Repair (3)

- Needs Assessment (5)
- Repair Needed (37)
- In Progress (1)
- Completed - Ready for Inspection (1)
- Completed - Inspected (13)

- Contained
- Uncontained
- Wildfire Daily Fire Perimeter
- InteriorRoads
- Secondary Highway
- Paved Roads
- Dirt (Not Paved)
- Paved Road
- Gravel Road
- Dirt Roads
- Unimproved Roads
- Closed Roads
- Wilderness
- Roadless Area

Note: This map and associated tables have been filtered to only show Repair Points / Lines of Medium or High priority. There exists numerous other features of unknown or low priority repair needs throughout the fire area. The intended use of this map is to define/represent the repair work to be completed during IMT12 oversight of this incident. This map should ***NOT*** be considered a complete source for repair information.

Div P2

0 1 Miles

map exported at 10/22/2022 1934 hrs

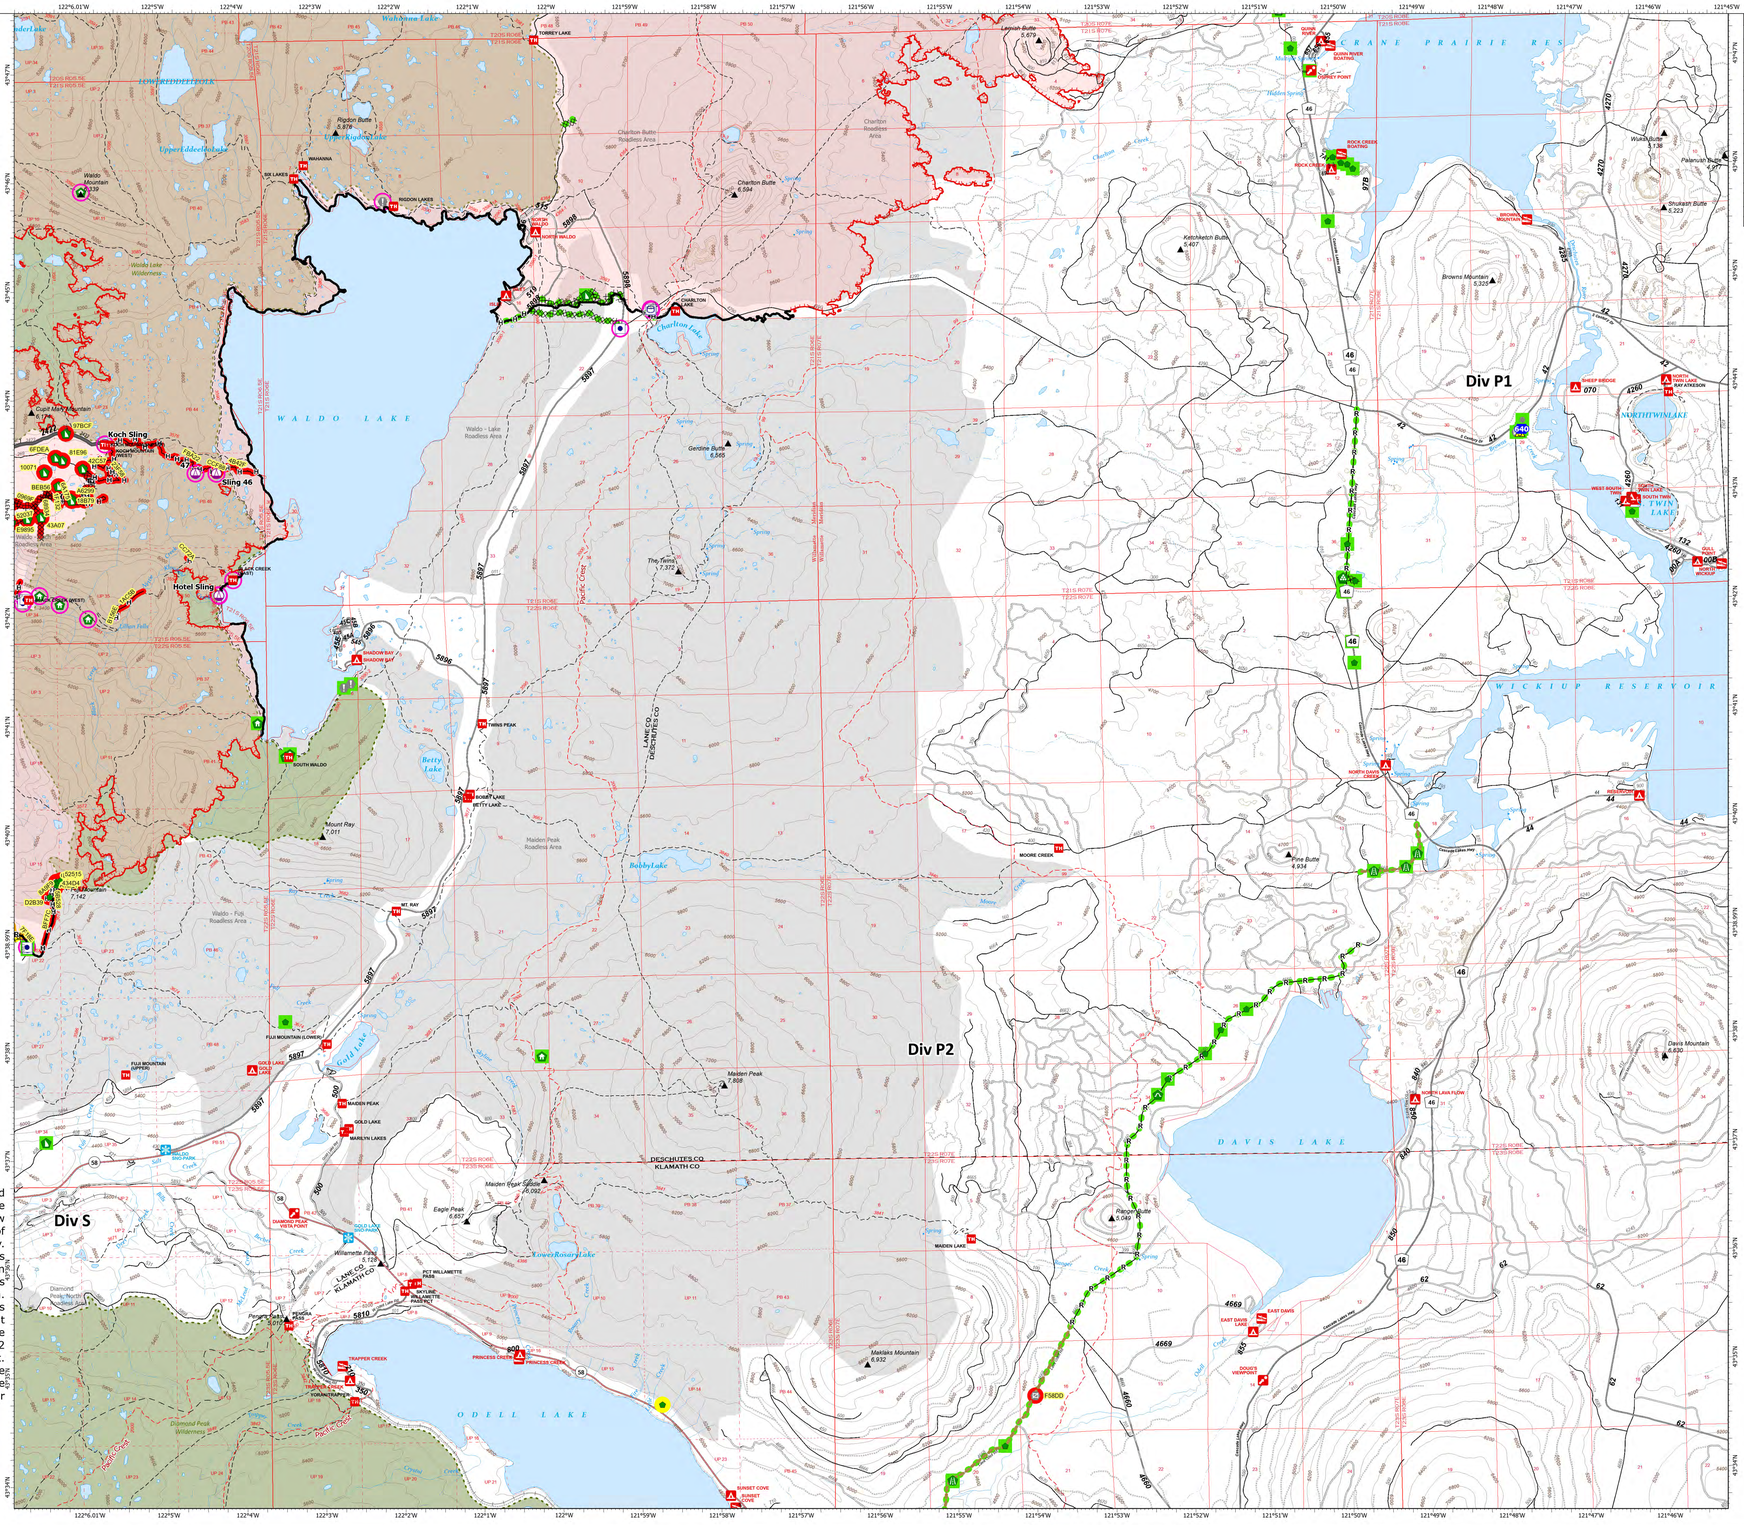

Repair ID	Priority	Point Type	Status	Repairs Needed	Repair Comments	Latitude	Longitude
97BCF	High	Dozer Push	Repair Needed	FULL REPAIR	400 ft x 150. Seed and mulch. Pull back slash and berms. Ask Forest how large than trailhead was before dozer work. 8/29 KBB	43° 43.696' N	122° 06.159' W
A02A1	High	Repair Point	Repair Needed	Pull in berms, fill trench, dispulse entrances, cover with slash, water bar as needed		43° 39.542' N	122° 06.339' W
B8F28	High	Repair Point	Repair Needed	Pull in berms, cover in slash, dispulse entrances (REAF Johannsen 10/5)		43° 39.571' N	122° 06.314' W
424D4	High	Repair Point	Repair Needed	FULL REPAIR. Pull in berms, cover in slash, dispulse entrances, water bar as needed (REAF Johannsen 10/5)		43° 39.560' N	122° 06.309' W
5D925	High	Repair Point	Repair Needed	FULL REPAIR. Pull in berms, cover in slash, dispulse entrances, water bar as needed (REAF Johannsen 10/5)		43° 39.560' N	122° 06.298' W
02B59	High	Repair Point	Repair Needed	FULL REPAIR. Pull in berm; distribute slash to more natural levels. Trail needs Rec specialist (Johannsen 10/5)		43° 39.410' N	122° 06.415' W
16071	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	43° 43.340' N	122° 06.410' W
9E95G	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	43° 43.211' N	122° 06.259' W
A6299	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	43° 43.050' N	122° 06.105' W
38679	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	43° 43.078' N	122° 06.094' W
43A97	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	43° 42.927' N	122° 06.402' W
E9895	Medium	Dozer Push	Repair Needed		Disperse soil and slash	43° 42.911' N	122° 06.659' W
9E096	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back berm disperse remaining slash	43° 43.448' N	122° 06.206' W
4DC57	Medium	Dozer Push	Repair Needed	FULL REPAIR	Large boulders on site no slash.	43° 43.170' N	122° 05.940' W
9FDEA	Medium	Dozer Push	Repair Needed	FULL REPAIR	Pull back material and disperse slash	43° 43.472' N	122° 06.292' W
F58D0	Medium	Gate	Repair Needed	Close Gate and secure with new Yale lock once approved by ops, REAF JOHNNSON 10/18.		43° 34.710' N	121° 54.013' W
D4A4D	Medium	Repair Point	Repair Needed	LIGHT REPAIR NEEDED	REAF BERG 9/22. Pull back berm to trail and naturalize.	43° 39.559' N	122° 06.311' W
C8217	Medium	Repair Point	Repair Needed	FULL REPAIR. Distribute slash to more natural levels		43° 39.537' N	122° 06.340' W

Repair ID	Priority	Line Type	Status	Repairs Needed	Repair Comments	Len (ft)
D0817	High	Completed Dozer Line	Repair Needed	Yes	Tie-in with retardant drop. Line is approximate. Repair dozer per forest standards.	907
20942	High	Completed Dozer Line	Repair Needed	FULL REPAIR	Repair to standard	1554
68934	High	Completed Dozer Line	Repair Needed	FULL REPAIR		3402
186JC	High	Completed Dozer Line	Repair Needed	FULL REPAIR		259
57D04	High	Completed Dozer Line	Repair Needed	Yes	Repair to standard	184
A16D1	High	Completed Dozer Line	Repair Needed	Yes	Repair to standard	185
8926	High	Completed Dozer Line	Repair Needed	FULL REPAIR	Pull back berms, seed and mulch. J Hoganson 8/30	732
0969F	High	Completed Dozer Line	Repair Needed	FULL REPAIR	Pull back berms, slash and logs. Seed and mulch. J Hoganson 8/30.	3361
52037	High	Completed Dozer Line	Repair Needed	FULL REPAIR	Pull berms, cover with slash	1010
3F150	High	Completed Dozer Line	Repair Needed	FULL REPAIR	Pull back berms, logs and slash. Seed and mulch. J Hoganson 8/31	621
4B42F	High	Completed Hand Line	Repair Needed	pull flagging. pull hose lay. -disperse large piles of stumps,low stumping, pull back berms and cups, disperse green material across scratch		3867
CCF88	High	Completed Hand Line	Repair Needed	FULL REPAIR	pull flagging.pull hose lay - disperse large piles of stumps,low stumping, pull back berms and cups, disperse green material across scratch	1852
15B22	High	Completed Hand Line	Repair Needed	FULL REPAIR	pull flagging.pull hose lay - disperse large piles of stumps,low stumping, pull back berms and cups, disperse green material across scratch	3923
23F58	High	Completed Hand Line	Repair Needed	FULL REPAIR	Repair to standard	4514
220F3	High	Completed Hand Line	Repair Needed	FULL REPAIR	Repair to standard	2226
C8675	High	Completed Hand Line	Repair Needed	FULL REPAIR		196
6E96C	High	Completed Hand Line	Repair Needed	FULL REPAIR		281
EA71F	High	Completed Hand Line	Repair Needed	FULL REPAIR		2633
27703	High	Completed Hand Line	Repair Needed	FULL REPAIR		482
C8D13	High	Completed Hand Line	Repair Needed	FULL REPAIR		1052

Repair ID	Priority	Line Type	Status	Repairs Needed	Repair Comments	Len (ft)
95AD8	High	Completed Hand Line	Repair Needed	FULL REPAIR		230
9C5G7	High	Completed Hand Line	Repair Needed	FULL REPAIR		404
A4E41	High	Completed Hand Line	Repair Needed	FULL REPAIR		198
20184	High	Completed Hand Line	Repair Needed	FULL REPAIR	Pull hose off line. Place slash back over p line and fire edge to make line unnoticeable. J Hoganson 8/31	4973
6AJ75	High	Completed Hand Line	Repair Needed	FULL REPAIR		1409
F3965	High	Completed Hand Line	Repair Needed	130FT REPAIR to prevent all routes. Disperse slash - REW/ARCH ROOD 9-18; Pull in berms, fill trench, cover in slash, dispulse entrance, water bar as needed.	Disperse slash and cut rounds piled on the green side fo more natural levels (REAF Johannsen)	669
5B5J8	High	Completed Hand Line	Repair Needed	FULL REPAIR	Pull in berms, fill in trench, cover with slash, add water bars, dispulse the entrances (REAF Johannsen 10/5)	935
19303	High	Completed Hand Line	Repair Needed	FULL REPAIR	Pull in berms, fill in trench, cover with slash, dispulse entrances, add water bars,	221
B48F9	High	Completed Hand Line	Repair Needed	FULL REPAIR	REAF Johannsen 10/5 Pull in berms, fill trench, dispulse entrances, cover with slash, water bar as needed	496
1C5C7	High	Completed Road as Line	Repair Needed	Pull in berms and slash, close with boulders.	close with boulders because the road is unsafe for vehicle traffic. J Hoganson 9/23	770
A1F99	Medium	Completed Dozer Line	Repair Needed	FULL REPAIR	FULL REPAIR	138
8AA4C	Medium	Completed Hand Line	Needs Assessment			331
A3F01	Medium	Completed Hand Line	Needs Assessment			13
03923	Medium	Completed Hand Line	Needs Assessment			38
B19AE	Medium	Completed Hand Line	Needs Assessment			22
2E3EC	Medium	Completed Hand Line	Repair Needed	FULL REPAIR		367
C272A	Medium	Completed Hand Line	Repair Needed	FULL REPAIR		214
CAFD9	Medium	Completed Hand Line	Repair Needed	FULL REPAIR		173
1AC5B	Medium	Completed Hand Line	Repair Needed	FULL REPAIR		2102
8FF7C	Medium	Completed Hand Line	Repair Needed	Consult with local recreation folks for future trail repair. REAF GRANT 10/5: scatter slash and rounds to a more natural density, trail tread should be assessed by recreation for repair needs.		3550
