


STRATEGIC PLANNING

BULL COMPLEX

OR-MHF-000753

9/3/2021 DAY

13,194 ACRES AT 09/02/2021 @ 2037

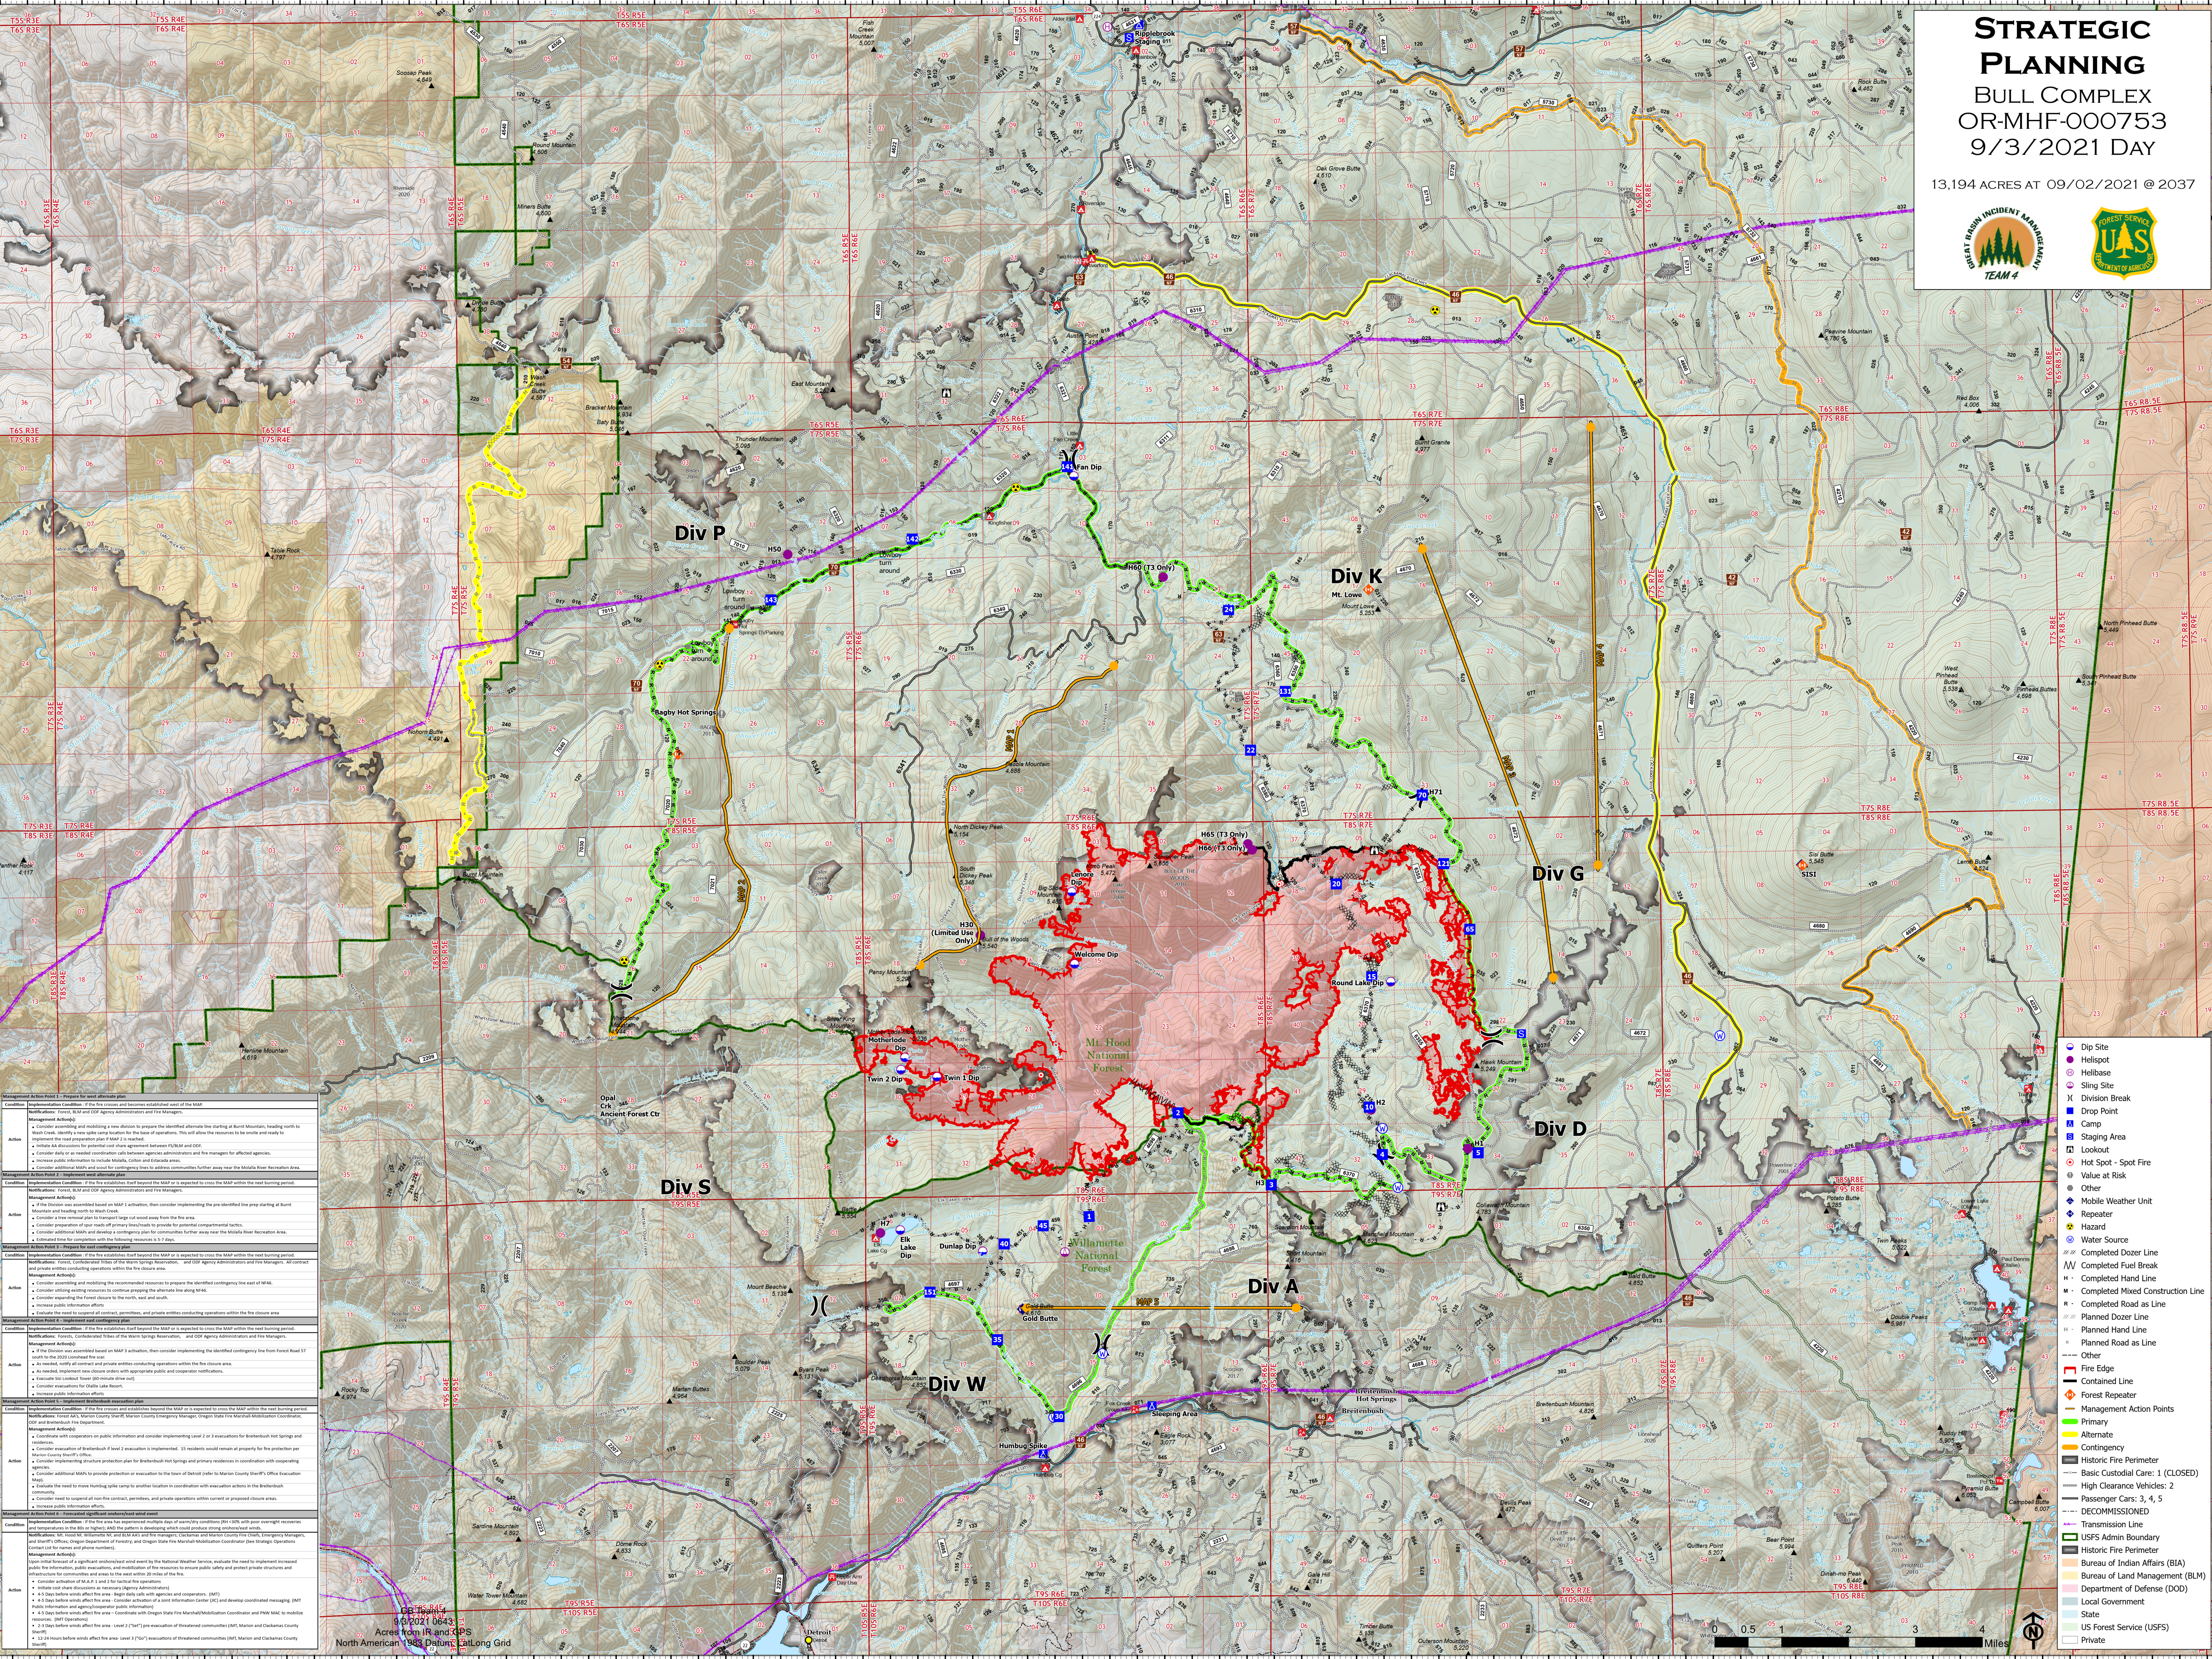

Management Action Point	Location	Implementation Conditions	Management Activities	Action
Management Action Point 1 - Prepare for west alternate plan	Implementation Conditions: If the fire crosses and becomes established west of the MAAP	Management Activities: USFS and COP Agency Administrators and Fire Managers	<ul style="list-style-type: none"> Consider assessing and mobilizing a new division to prepare the identified alternate fire starting at Mount Marston, heading north to West Creek. Identify a safe area for the start of operations. This will allow the resources to be on-site and ready to improve the fuel preparation plan if MAAP 2 is reached. Consider a fire removal plan to transport fuel out west from the fire area. Consider preparation of a new route off primary roads to provide for extended operational tactics. Consider additional MAAP and local contingency plan for communities further west near the Multa River Recreation Area. Consider additional MAAP and local contingency plan to address communities further west near the Multa River Recreation Area. 	<ul style="list-style-type: none"> Consider assessing and mobilizing the recommended resources to prepare the identified contingency west of MAAP. Consider setting up fire resources to improve prep work along the line. Consider expanding the fire closure to the north, east and south. Increase public information efforts. Prepare the road to support all contract, permits, and private entities conducting operations within the fire closure area.
Management Action Point 2 - Prepare for east alternate plan	Implementation Conditions: If the fire crosses and becomes established east of the MAAP within the next burning period	Management Activities: Forest, BIA, and COP Agency Administrators and Fire Managers	<ul style="list-style-type: none"> If the Division was established based on MAAP 3 activation, then consider implementing the pre-identified fire prep starting at Mount Marston and heading north to West Creek. Consider a fire removal plan to transport fuel out west from the fire area. Consider preparation of a new route off primary roads to provide for extended operational tactics. Consider additional MAAP and local contingency plan for communities further west near the Multa River Recreation Area. Consider additional MAAP and local contingency plan to address communities further west near the Multa River Recreation Area. 	<ul style="list-style-type: none"> Consider assessing and mobilizing the recommended resources to prepare the identified contingency east of MAAP. Consider setting up fire resources to improve prep work along the line. Consider expanding the fire closure to the north, east and south. Increase public information efforts. Prepare the road to support all contract, permits, and private entities conducting operations within the fire closure area.
Management Action Point 3 - Implement east contingency plan	Implementation Conditions: If the fire crosses and becomes established east of the MAAP within the next burning period	Management Activities: Forest, BIA, and COP Agency Administrators and Fire Managers	<ul style="list-style-type: none"> If the Division was established based on MAAP 3 activation, then consider implementing the pre-identified contingency line from Forest Road 57 south to the 2020 contour fire line. As needed, mobilize and create units within conducting operations within the fire closure area. As needed, implement new closure orders with appropriate public and cooperative notifications. Consider additional MAAP and local contingency plan for communities further west near the Multa River Recreation Area. Consider additional MAAP and local contingency plan to address communities further west near the Multa River Recreation Area. 	<ul style="list-style-type: none"> Consider assessing and mobilizing the recommended resources to prepare the identified contingency east of MAAP. Consider setting up fire resources to improve prep work along the line. Consider expanding the fire closure to the north, east and south. Increase public information efforts. Prepare the road to support all contract, permits, and private entities conducting operations within the fire closure area.
Management Action Point 4 - Implement west contingency plan	Implementation Conditions: If the fire crosses and becomes established west of the MAAP within the next burning period	Management Activities: Forest, BIA, and COP Agency Administrators and Fire Managers	<ul style="list-style-type: none"> If the Division was established based on MAAP 3 activation, then consider implementing the pre-identified contingency line from Forest Road 57 south to the 2020 contour fire line. As needed, mobilize and create units within conducting operations within the fire closure area. As needed, implement new closure orders with appropriate public and cooperative notifications. Consider additional MAAP and local contingency plan for communities further west near the Multa River Recreation Area. Consider additional MAAP and local contingency plan to address communities further west near the Multa River Recreation Area. 	<ul style="list-style-type: none"> Consider assessing and mobilizing the recommended resources to prepare the identified contingency west of MAAP. Consider setting up fire resources to improve prep work along the line. Consider expanding the fire closure to the north, east and south. Increase public information efforts. Prepare the road to support all contract, permits, and private entities conducting operations within the fire closure area.
Management Action Point 5 - Evacuate significant residential wild west	Implementation Conditions: If the fire has experienced multiple days of activity conditions (see table) with poor overnight resources	Management Activities: USFS, BIA, and COP Agency Administrators and Fire Managers	<ul style="list-style-type: none"> Coordinate with cooperators on public information and consider implementing Level 2 or 3 evacuations for Breitenbush Hot Springs and surrounding areas. Consider evacuation of Breitenbush 3 level 2 evacuation is implemented. 33 residents will remain at property for fire protection per Breitenbush Community Office. Consider engineering structure protection plan for Breitenbush Hot Springs and primary residences in coordination with cooperating agencies. Consider additional MAAP to provide protection or evacuation to the town of Detroit prior to Marion County Sheriff's Office (MCO) arrival. Consider the need to support all contract, permits, and private entities within current or proposed closure areas. Increase public information efforts. 	<ul style="list-style-type: none"> Coordinate with cooperators on public information and consider implementing Level 2 or 3 evacuations for Breitenbush Hot Springs and surrounding areas. Consider evacuation of Breitenbush 3 level 2 evacuation is implemented. 33 residents will remain at property for fire protection per Breitenbush Community Office. Consider engineering structure protection plan for Breitenbush Hot Springs and primary residences in coordination with cooperating agencies. Consider additional MAAP to provide protection or evacuation to the town of Detroit prior to Marion County Sheriff's Office (MCO) arrival. Consider the need to support all contract, permits, and private entities within current or proposed closure areas. Increase public information efforts.

- Dip Site
- Helispot
- Helibase
- Slings Site
- X Division Break
- Drop Point
- Camp
- Staging Area
- Lookout
- Hot Spot - Spot Fire
- Value at Risk
- Other
- Mobile Weather Unit
- Repeater
- Hazard
- Water Source
- Completed Dozer Line
- MV Completed Fuel Break
- Completed Hand Line
- M - Completed Mixed Construction Line
- R - Completed Road as Line
- Planned Dozer Line
- Planned Hand Line
- Planned Road as Line
- Other
- Contained Line
- Forest Repeater
- Management Action Points
- Primary
- Alternate
- Contingency
- Historic Fire Perimeter
- Basic Custodial Care: 1 (CLOSED)
- High Clearance Vehicles: 2
- Passenger Cars: 3, 4, 5
- DECOMMISSIONED
- Transmission Line
- USFS Admin Boundary
- Historic Fire Perimeter
- Bureau of Indian Affairs (BIA)
- Bureau of Land Management (BLM)
- Department of Defense (DOD)
- Local Government
- State
- US Forest Service (USFS)
- Private

Acres from IR and GPS
North American 1983 Datum, Callong Grid

